


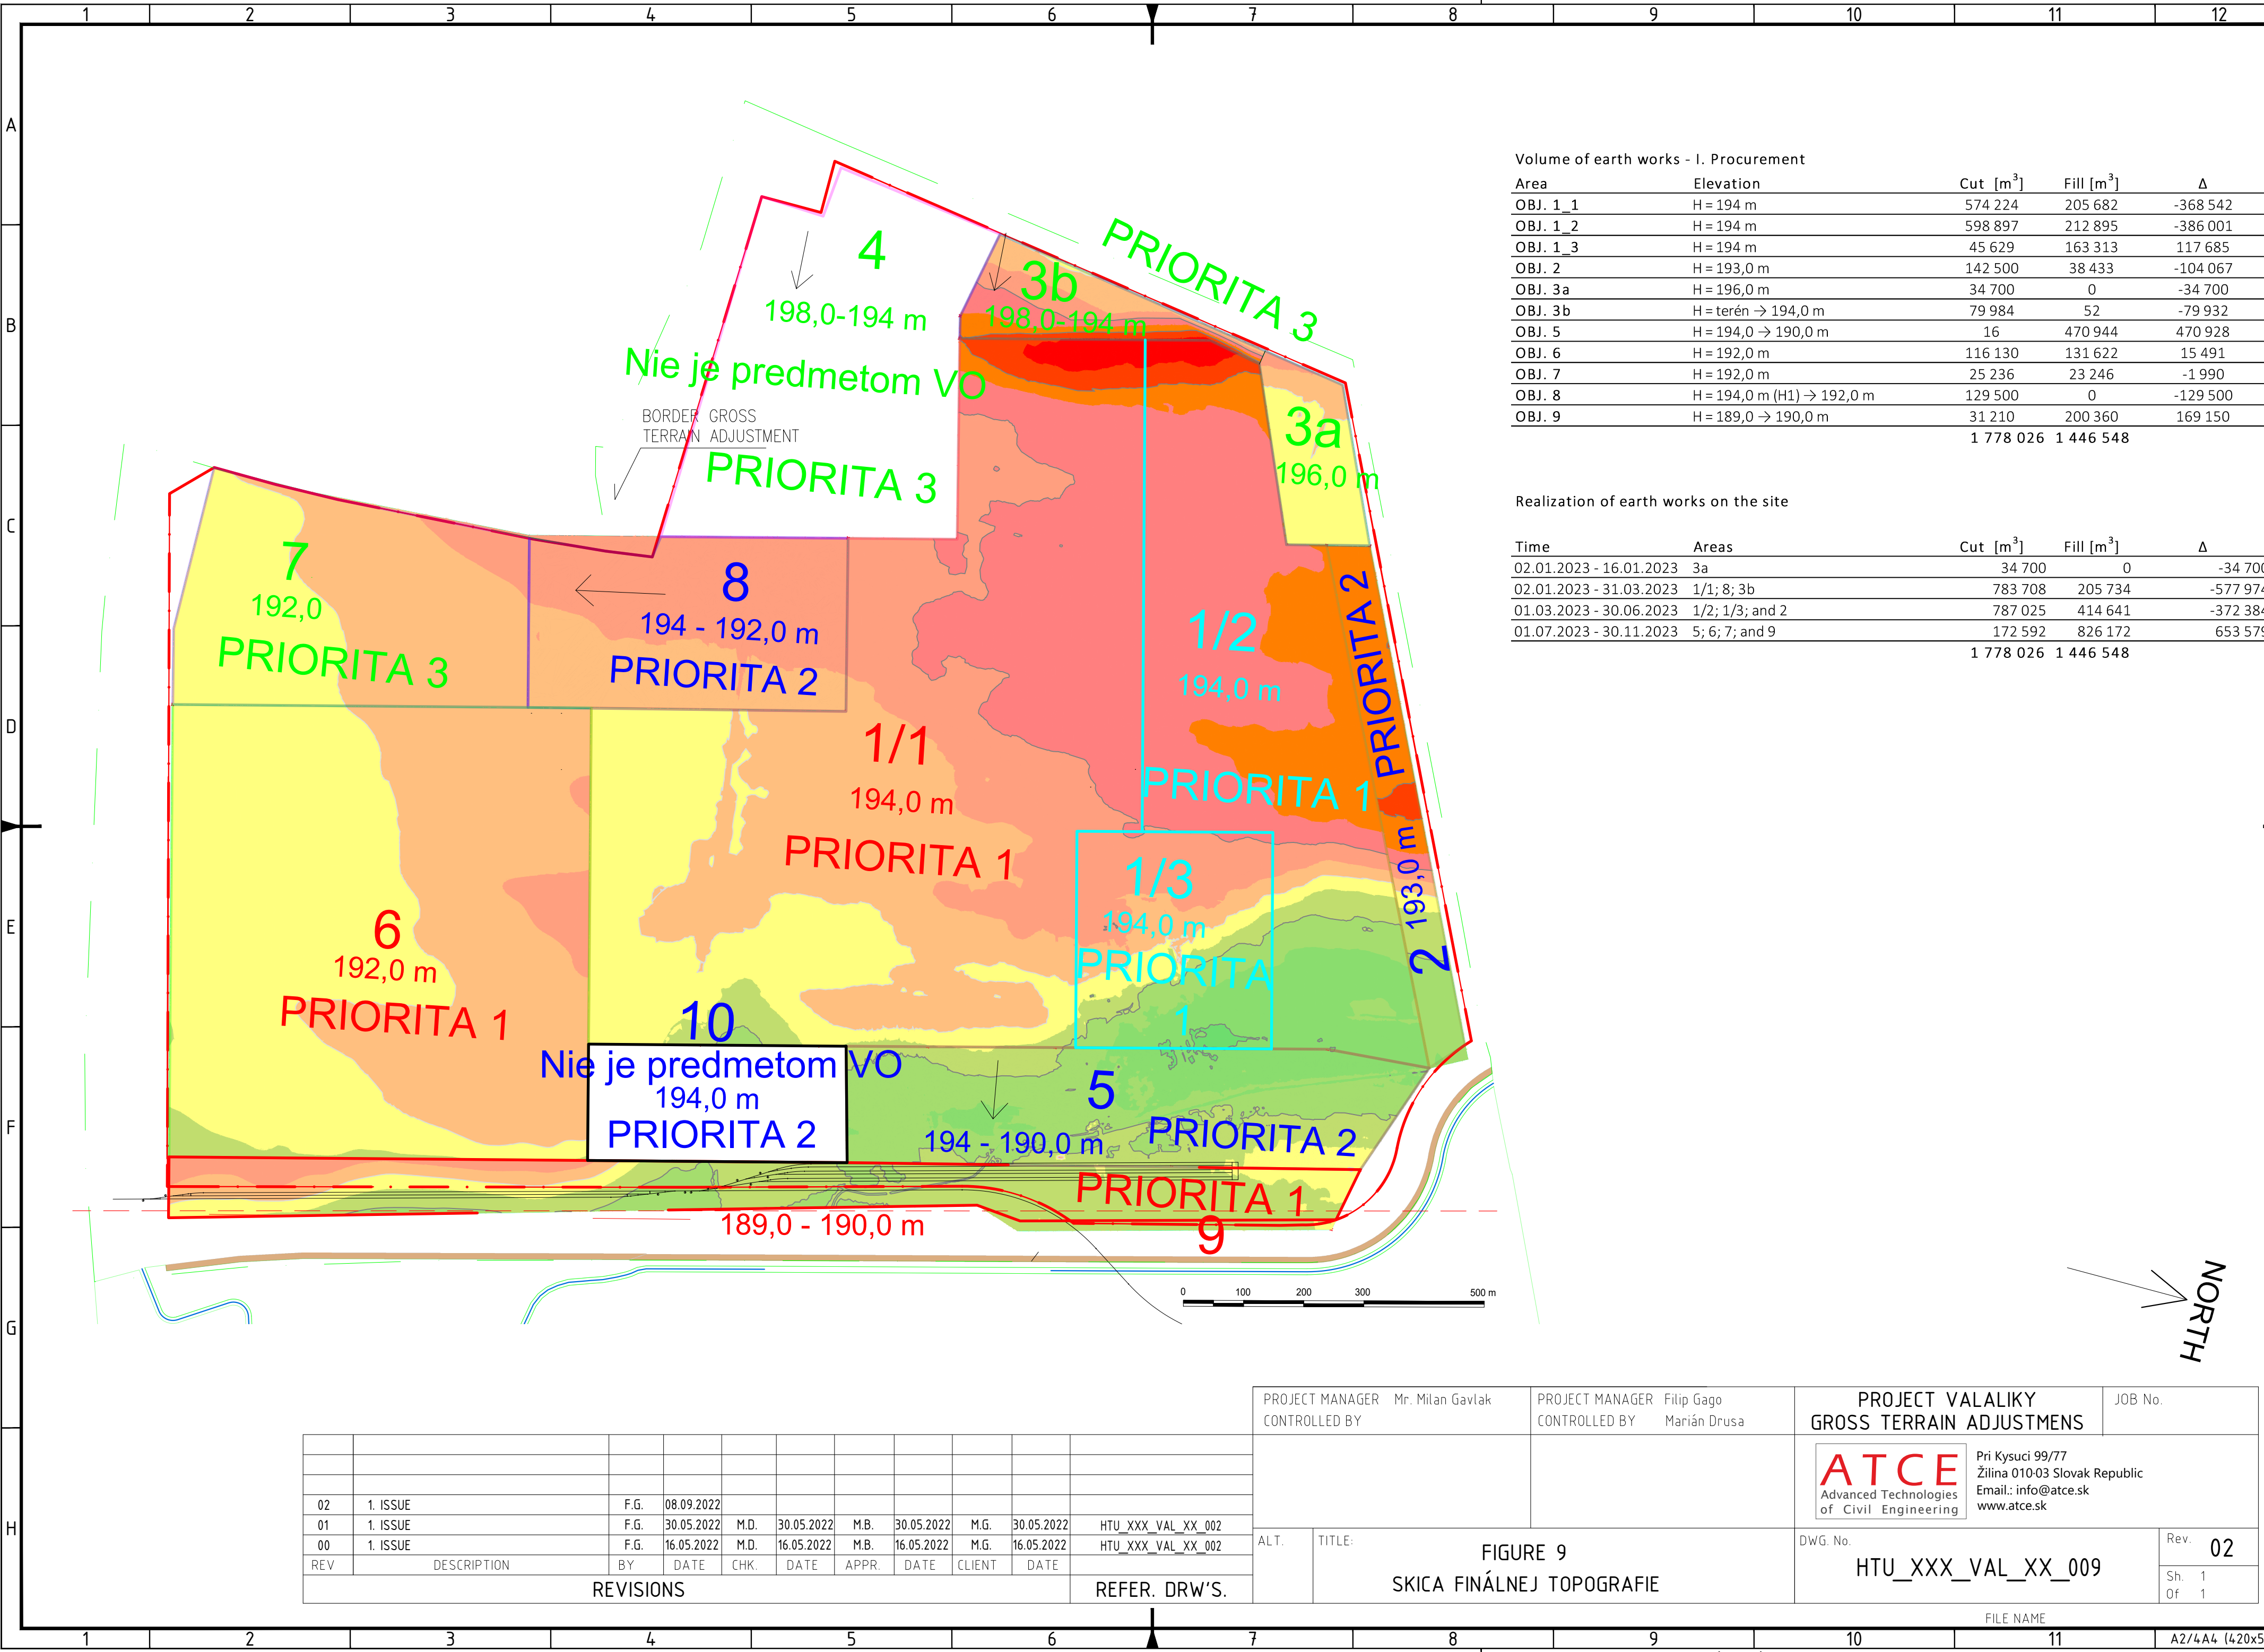

Volume of earth works - I. Procurement

Area	Elevation	Cut [m³]	Fill [m³]	Δ
OBJ. 1_1	H = 194 m	574 224	205 682	-368 542
OBJ. 1_2	H = 194 m	598 897	212 895	-386 001
OBJ. 1_3	H = 194 m	45 629	163 313	117 685
OBJ. 2	H = 193,0 m	142 500	38 433	-104 067
OBJ. 3a	H = 196,0 m	34 700	0	-34 700
OBJ. 3b	H = terén → 194,0 m	79 984	52	-79 932
OBJ. 5	H = 194,0 → 190,0 m	16	470 944	470 928
OBJ. 6	H = 192,0 m	116 130	131 622	15 491
OBJ. 7	H = 192,0 m	25 236	23 246	-1 990
OBJ. 8	H = 194,0 m (H1) → 192,0 m	129 500	0	-129 500
OBJ. 9	H = 189,0 → 190,0 m	31 210	200 360	169 150
		1 778 026	1 446 548	

Realization of earth works on the site

Time	Areas	Cut [m³]	Fill [m³]	Δ
02.01.2023 - 16.01.2023	3a	34 700	0	-34 700
02.01.2023 - 31.03.2023	1/1; 8; 3b	783 708	205 734	-577 974
01.03.2023 - 30.06.2023	1/2; 1/3; and 2	787 025	414 641	-372 384
01.07.2023 - 30.11.2023	5; 6; 7; and 9	172 592	826 172	653 579
		1 778 026	1 446 548	

REV	DESCRIPTION	BY	DATE	CHK.	DATE	APPR.	DATE	CLIENT	DATE	REFER. DRW'S.
02	1. ISSUE	F.G.	08.09.2022							
01	1. ISSUE	F.G.	30.05.2022	M.D.	30.05.2022	M.B.	30.05.2022	M.G.	30.05.2022	HTU_XXX_VAL_XX_002
00	1. ISSUE	F.G.	16.05.2022	M.D.	16.05.2022	M.B.	16.05.2022	M.G.	16.05.2022	HTU_XXX_VAL_XX_002
REVISIONS										

PROJECT MANAGER Mr. Milan Gavlak CONTROLLED BY		PROJECT MANAGER Filip Gago CONTROLLED BY Marián Drusa		PROJECT VALALIKY GROSS TERRAIN ADJUSTMENS		JOB No.	
				ATCE Advanced Technologies of Civil Engineering Pri Kysuci 99/77 Žilina 010-03 Slovak Republic Email.: info@atce.sk www.atce.sk			
ALT.	TITLE: FIGURE 9 SKICA FINÁLNEJ TOPOGRAFIE			DWG. No. HTU_XXX_VAL_XX_009		Rev. 02	
						Sh. 1 Of 1	
